


ID	Task Name	Duration	Start	Finish	17, '01							Jun 24, '01							Jul 1, '01							Jul 8, '01						
					M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	
1	Cheetah	1152 hrs	Mon 1/8/01	Fri 7/27/01																												
2	Pre-Alpha Efforts	568 hrs	Mon 1/8/01	Mon 4/16/01																												
57	Alpha Builds 1 - 12 Tests	54 days	Tue 4/10/01	Fri 6/22/01																												
58	Server Down	23 hrs	Tue 6/26/01	Fri 6/29/01																												
59	Alpha Certification Build	0 hrs	Fri 6/29/01	Fri 6/29/01																												
60	Alpha Certification Build #2	0 hrs	Thu 7/5/01	Thu 7/5/01																												
66	Mike out sick	8 hrs	Tue 7/10/01	Tue 7/10/01																												
67	Jake out sick	8 hrs	Fri 7/13/01	Fri 7/13/01																												
68	Client Alpha Candidate	136 hrs	Thu 7/5/01	Fri 7/27/01																												
1	Alpha Certification Test Suites	136 hrs	Thu 7/5/01	Fri 7/27/01																												
2	White box tests COM compoents	80 hrs	Thu 7/5/01	Wed 7/18/01																												
3	Alpha Certification Build #2	0 hrs	Thu 7/5/01	Thu 7/5/01																												
5	Win98	12 hrs	Thu 7/5/01	Fri 7/6/01																												
6	Win 2000	12 hrs	Fri 7/6/01	Mon 7/9/01																												
7	ME	8 hrs	Tue 7/10/01	Tue 7/10/01																												
8	NT	12 hrs	Tue 7/17/01	Wed 7/18/01																												
9	Test Configuration B Win98	36.5 hrs	Thu 7/5/01	Wed 7/11/01																												
10	Sub suite tests: Win98 OEM IE 5.5	12.5 hrs	Thu 7/5/01	Fri 7/6/01																												
11	Sub suite tests: Second Edition IE 5.5	12.25 hrs	Fri 7/6/01	Mon 7/9/01																												
12	Sub suite tests: Win ME IE 5.5	13.25 hrs	Mon 7/9/01	Wed 7/11/01																												
13	Test Configuration C	58 hrs	Wed 7/18/01	Fri 7/27/01																												
14	Sub suite tests: Win98 SE IE 5.5	16 hrs	Wed 7/18/01	Thu 7/19/01																												
15	Sub suite tests: Win ME IE 5.5	40 hrs	Fri 7/20/01	Thu 7/26/01																												
16	Sub suite tests: Win2000 SP1 IE 5.5 (invalid cc	15 hrs	Mon 7/23/01	Wed 7/25/01																												
17	Sub suite tests: NT 4.0 SP 6A IE 5.5 (invalid cc	15 hrs	Wed 7/25/01	Fri 7/27/01																												
18	Test Configuration D	128 hrs	Thu 7/5/01	Thu 7/26/01																												
19	Sub suite tests: Win98 SE IE 5.5	40 hrs	Thu 7/5/01	Wed 7/11/01																												
20	Sub suite tests: Win ME IE 5.5	16 hrs	Wed 7/11/01	Thu 7/12/01																												
21	Sub suite tests: Win 98 SE IE 5.01	24 hrs	Tue 7/24/01	Thu 7/26/01																												
22	Sub suite tests: Win2000 SP1 IE 5.5	40 hrs	Thu 7/5/01	Wed 7/11/01																												
23	Sub suite tests: Win2000 SP1 IE 5.01	13 hrs	Thu 7/12/01	Fri 7/13/01																												
24	Sub suite tests: Win2000 SP2 IE 5.5	11 hrs	Fri 7/13/01	Mon 7/16/01																												
25	Sub suite tests: Win2000 SP2 IE 5.01	16 hrs	Mon 7/16/01	Tue 7/17/01																												
26	Sub suite tests: NT 4.0 SP 6A IE 5.01	24 hrs	Wed 7/18/01	Fri 7/20/01																												
27	Sub suite tests: NT 4.0 SP 6A IE 5.5	11.2 hrs	Fri 7/20/01	Mon 7/23/01																												
28	Test Configuration E	104 hrs	Wed 7/11/01	Fri 7/27/01																												
29	Full suite tests: Win98 SE IE 5.5	22.25 hrs	Wed 7/11/01	Thu 7/19/01																												
30	Full suite tests: Win ME IE 5.5	24 hrs	Mon 7/23/01	Wed 7/25/01																												

Start: Mon 1/8/01
 Tech Lead: Kevin Johnson
 Manager: William Gunkel

Task		Milestone		Planned Milestone	
Progress		Summary		Planned	

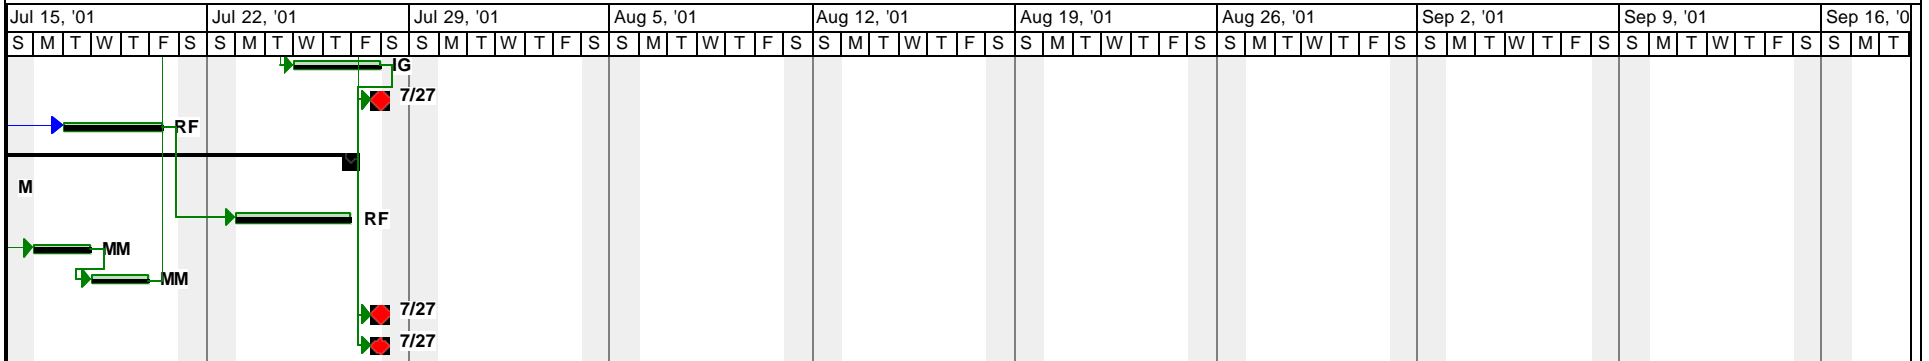

Start: Mon 1/8/01
 Tech Lead: Kevin Johnson
 Manager: William Gunkel

Task  Milestone  Planed Milestone 
 Progress  Summary  Planned 
